

SOUTHWEST

Green Line LRT Extension



Legislative Commission on Metropolitan Government

September 9, 2014




Today's Topics

- SWLRT Overview
- Municipal Consent Update
- Project Budget Update



Southwest LRT: Green Line Extension

- 16 miles
- 17 new stations
- Revenue service: 2019

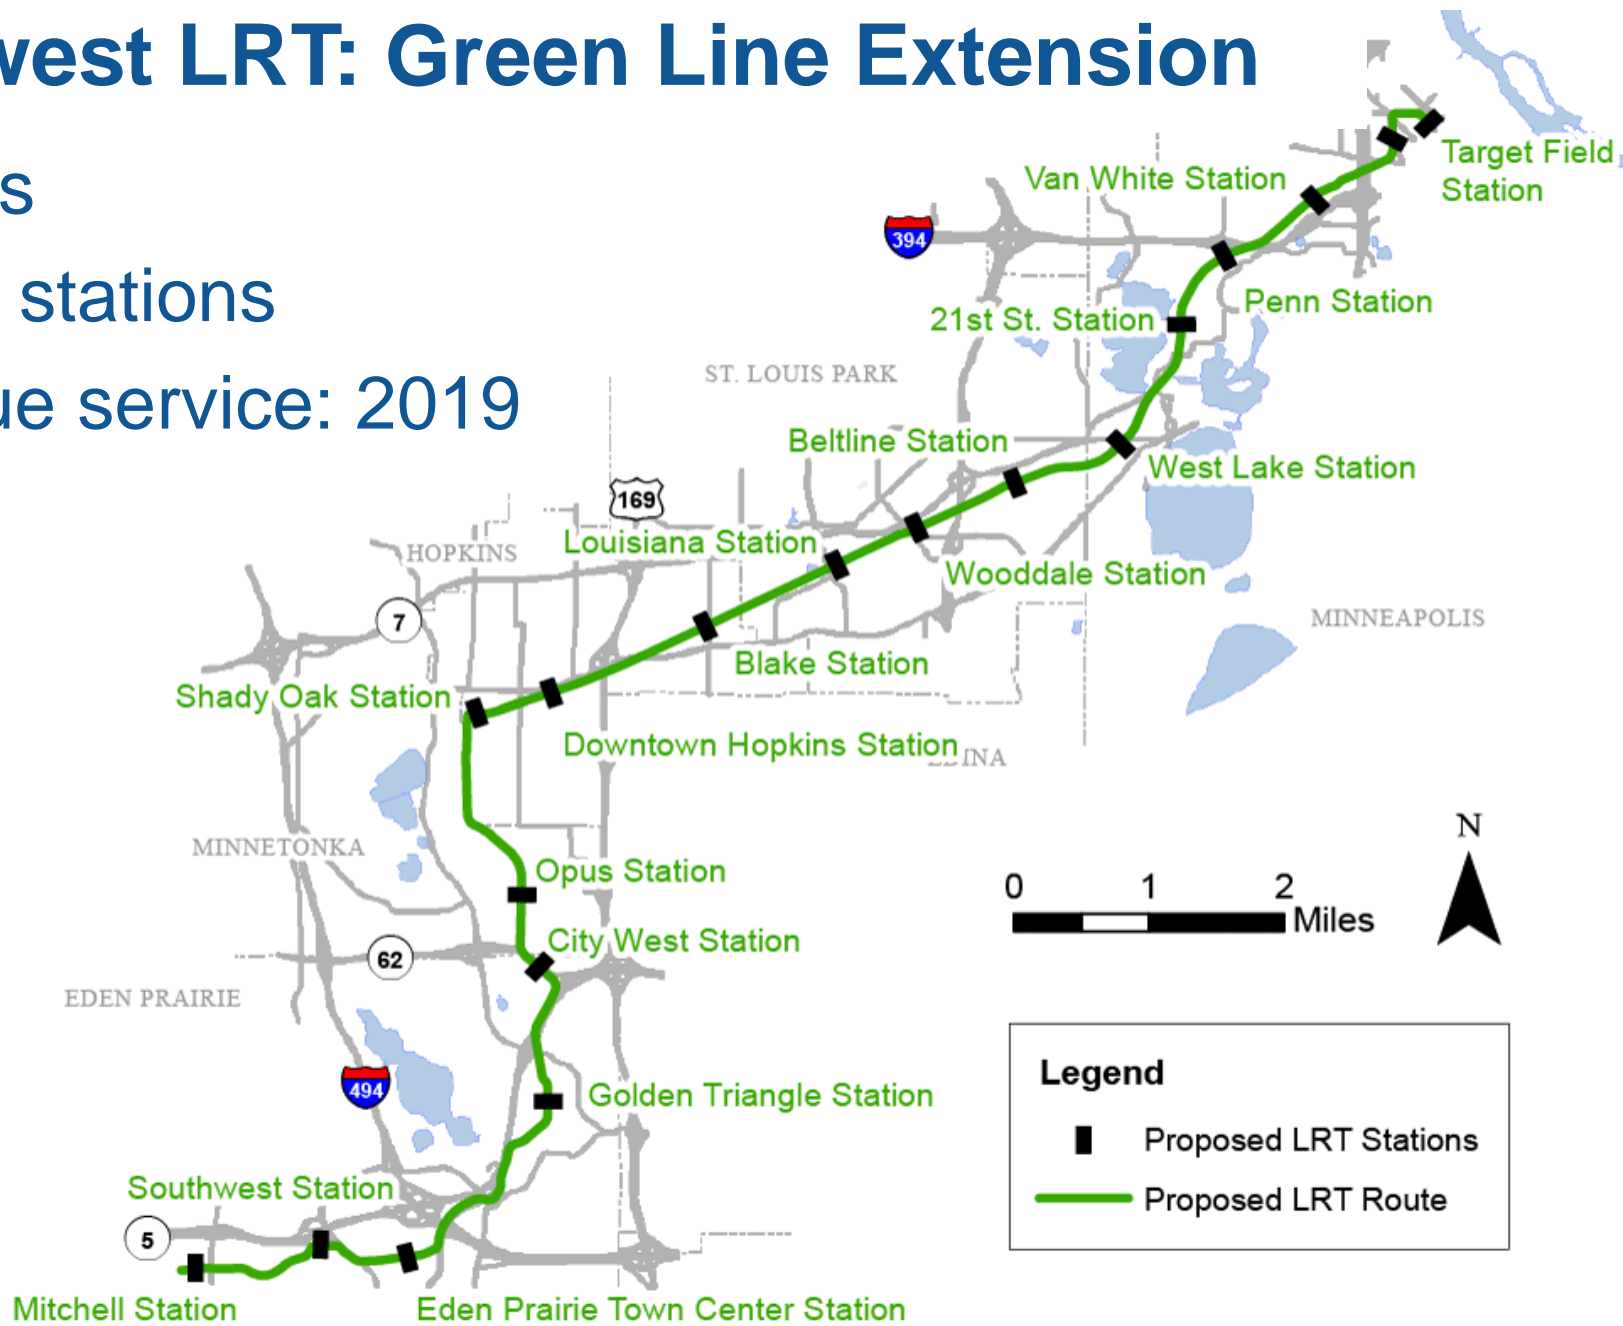

Southwest LRT Development Timeline

2013

- Project Development

2014

- Municipal Consent

2015

- Engineering, Supplemental DEIS, Final EIS

2016

- Full Funding Grant Agreement

2016-18

- Heavy Construction

2019

- Passenger Operations

Municipal Consent Update

Municipal Consent Hearings and Actions


Community	Public Hearing	Action	Passed
St. Louis Park	May 19	July 14	Yes
Eden Prairie	May 20	July 14	Yes
Joint Met Council & HCRRA	May 29	n/a	n/a
Minnetonka	June 2	June 23	Yes
Hopkins	June 3	June 17	Yes
Hennepin County	June 17	July 8	Yes*
Met Council/Hennepin County/HCRRA	August 13	n/a	n/a
Hennepin County	August 13	August 19	Yes**
Minneapolis	August 19	August 29	Yes

*Eden Prairie, Minnetonka, Hopkins & St. Louis Park

** Minneapolis Only


Project Budget Update

Current Project Budget: Sources of Funding

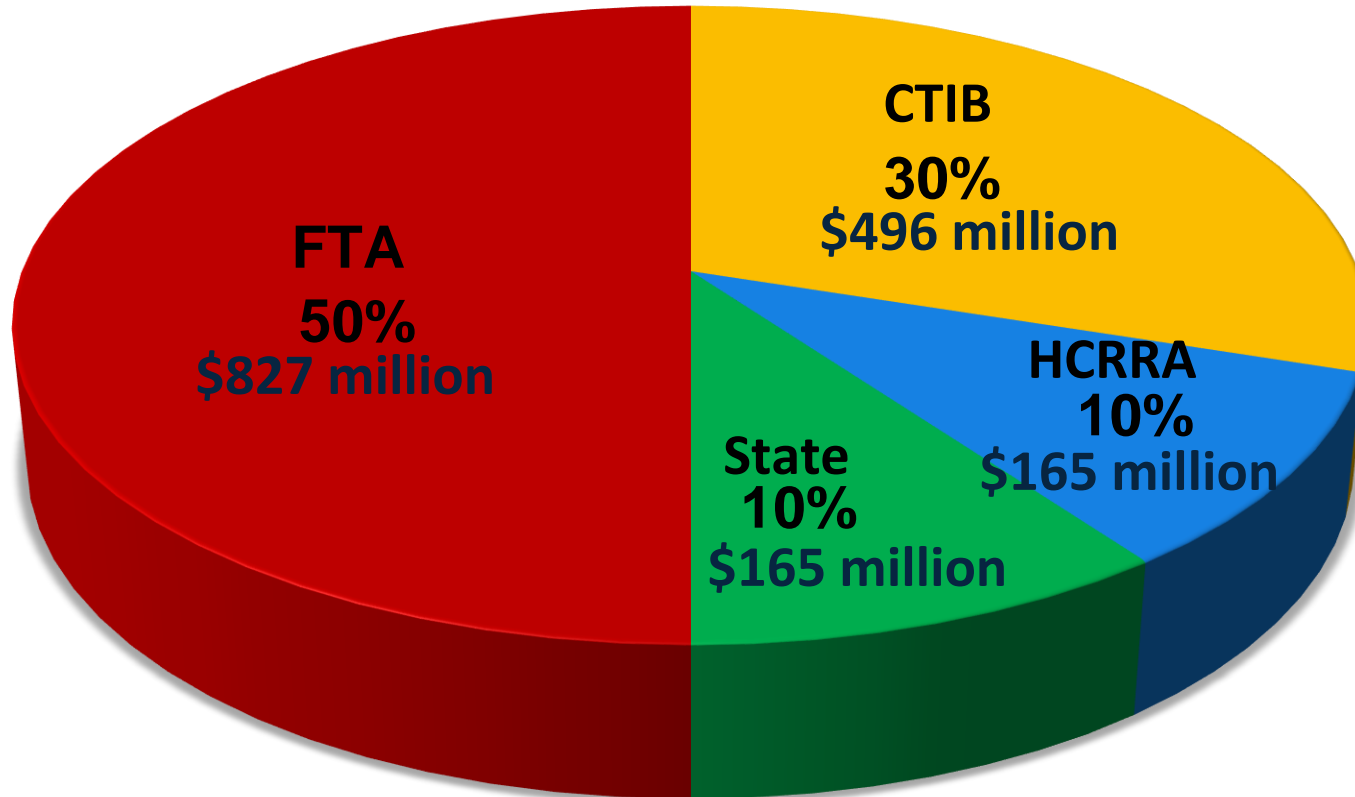

\$1.65 Billion

Current Project Budget: Committed Funds

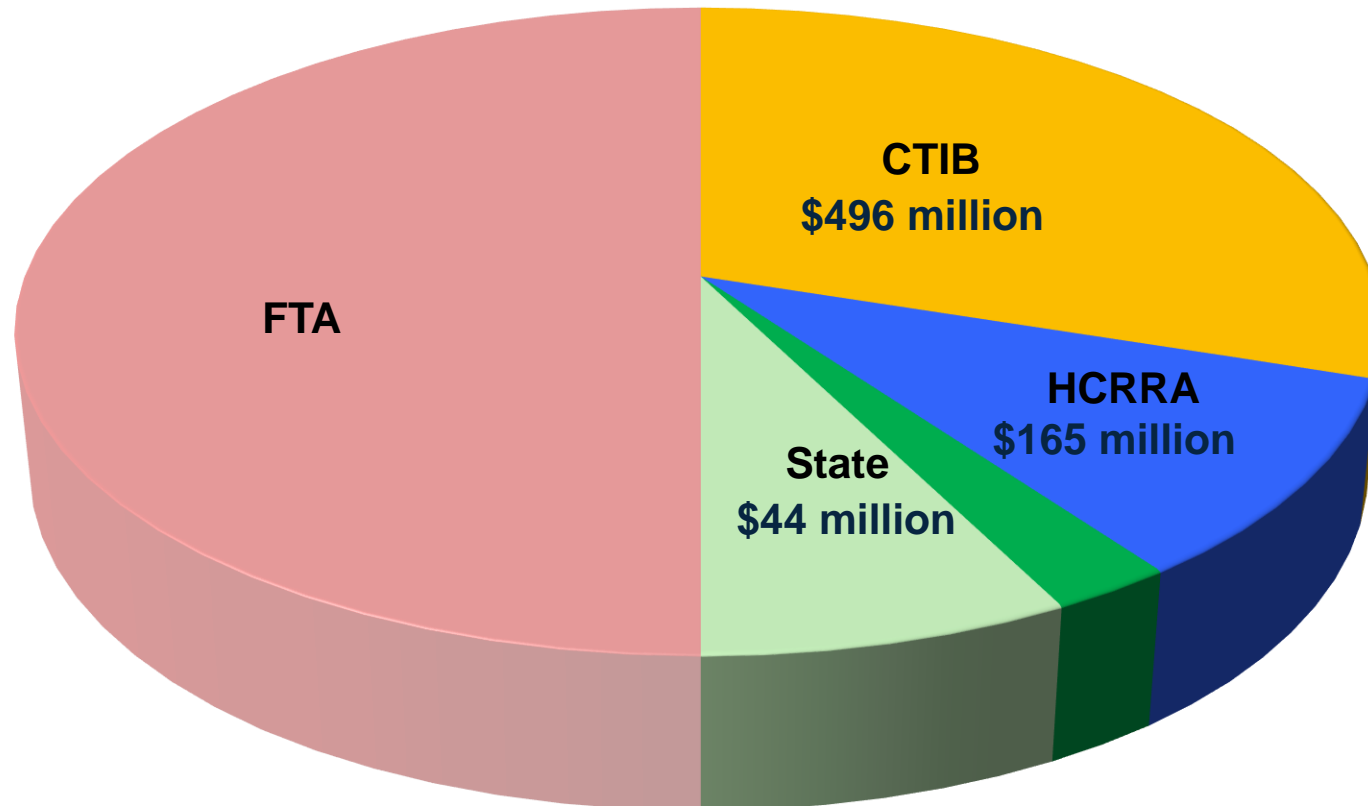

\$705 Million

More Information

Online:

www.SWLRT.org

Email:

SWLRT@metrotransit.org

Twitter:

www.twitter.com/southwestlrt

