

Central Corridor Light Rail Transit

Legislative Advisory Commission
Procurement Update
February 23, 2010

Mark Fuhrmann, Project Director



*Improving
mobility*


*Easing
congestion*

*Strengthening
our communities*

Central Corridor Light Rail Transit

Route and Stations

- 11 miles
- 18 new stations
- Over 40,000 projected riders per weekday by 2030

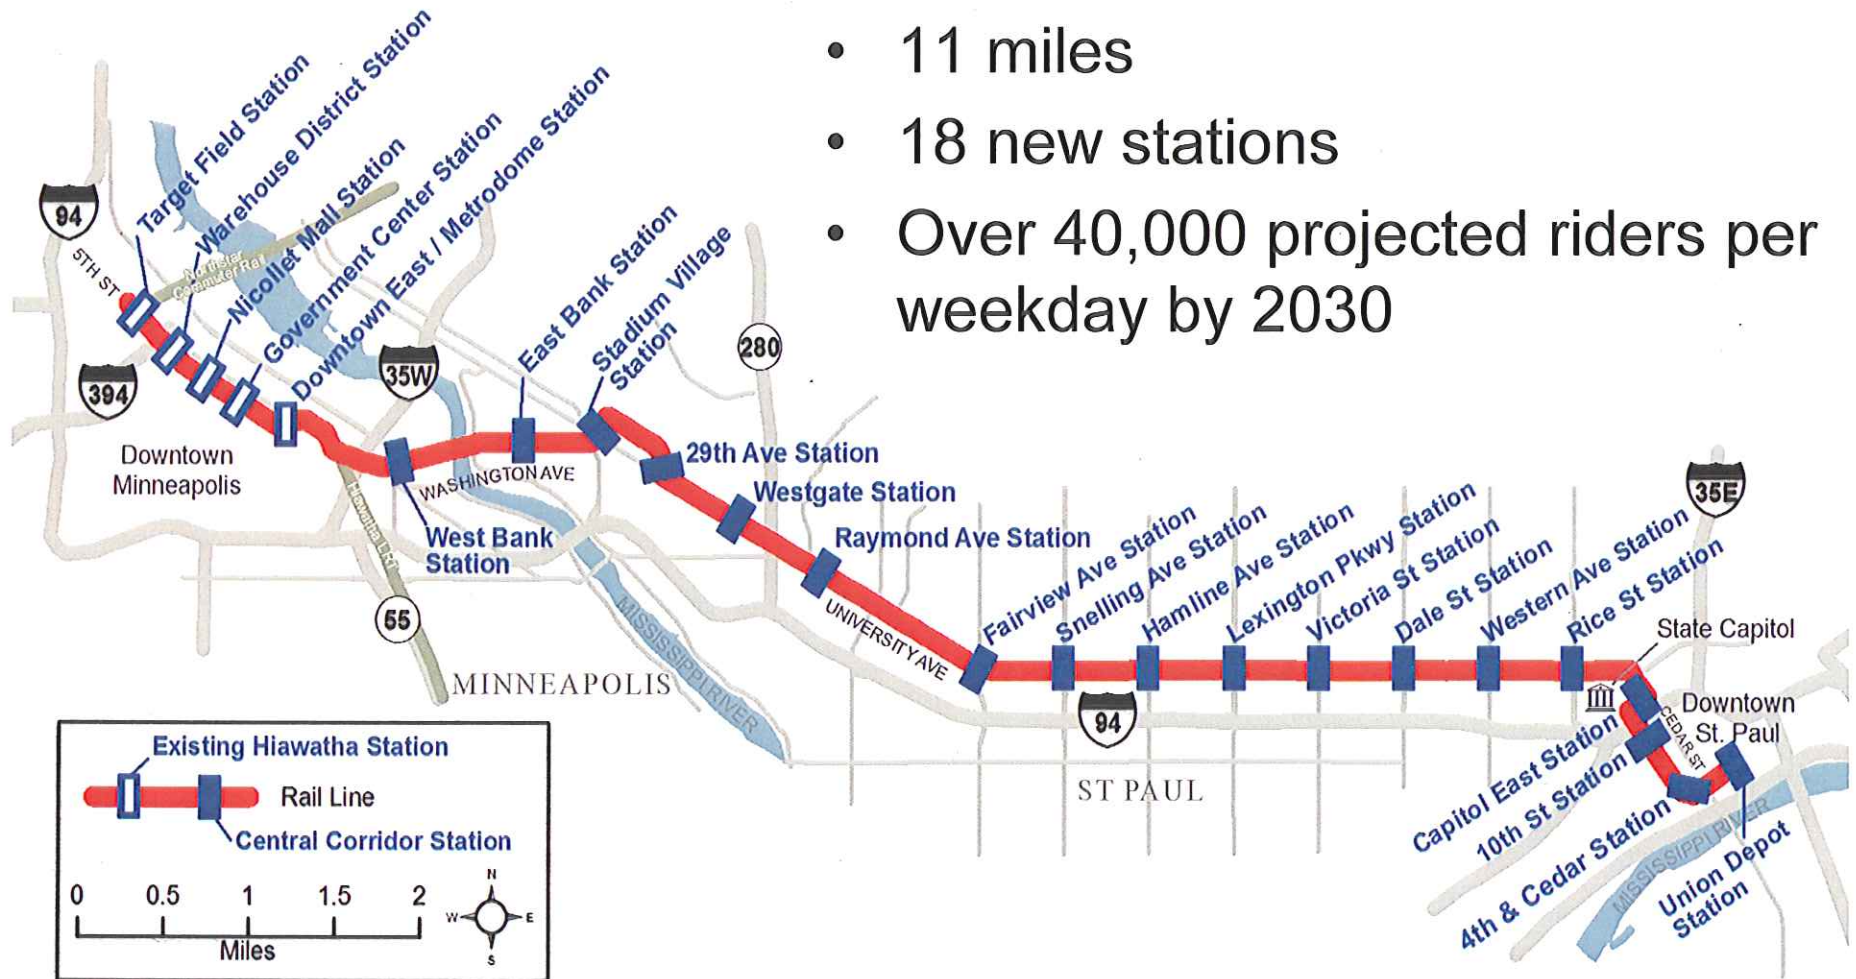

Series: 01_overview_color4

Central Corridor Light Rail Transit


Sources of Funds

Total Budget
\$957 Million

Ramsey Co.
\$66 million, 7%

Hennepin County
\$28 million, 3%


St. Paul
\$5 million, <1%

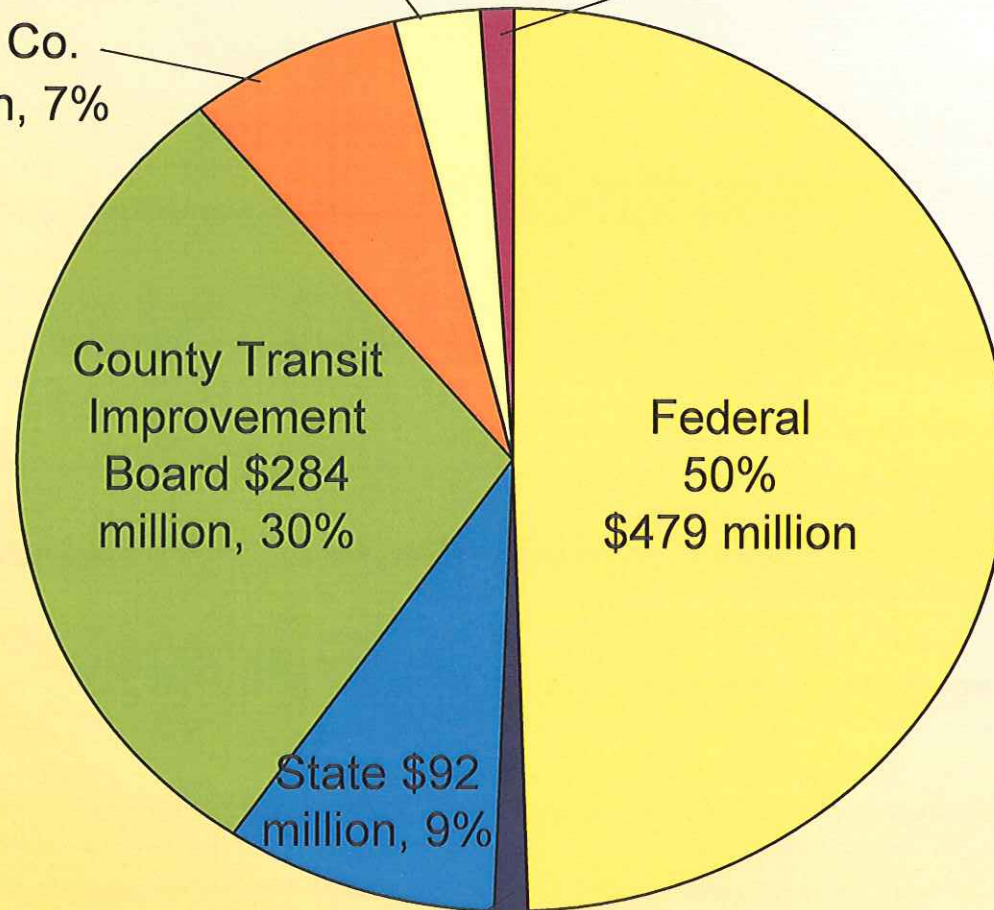

Central Corridor Light Rail Transit

**Total Budget
\$957 Million**

Uses of Funds

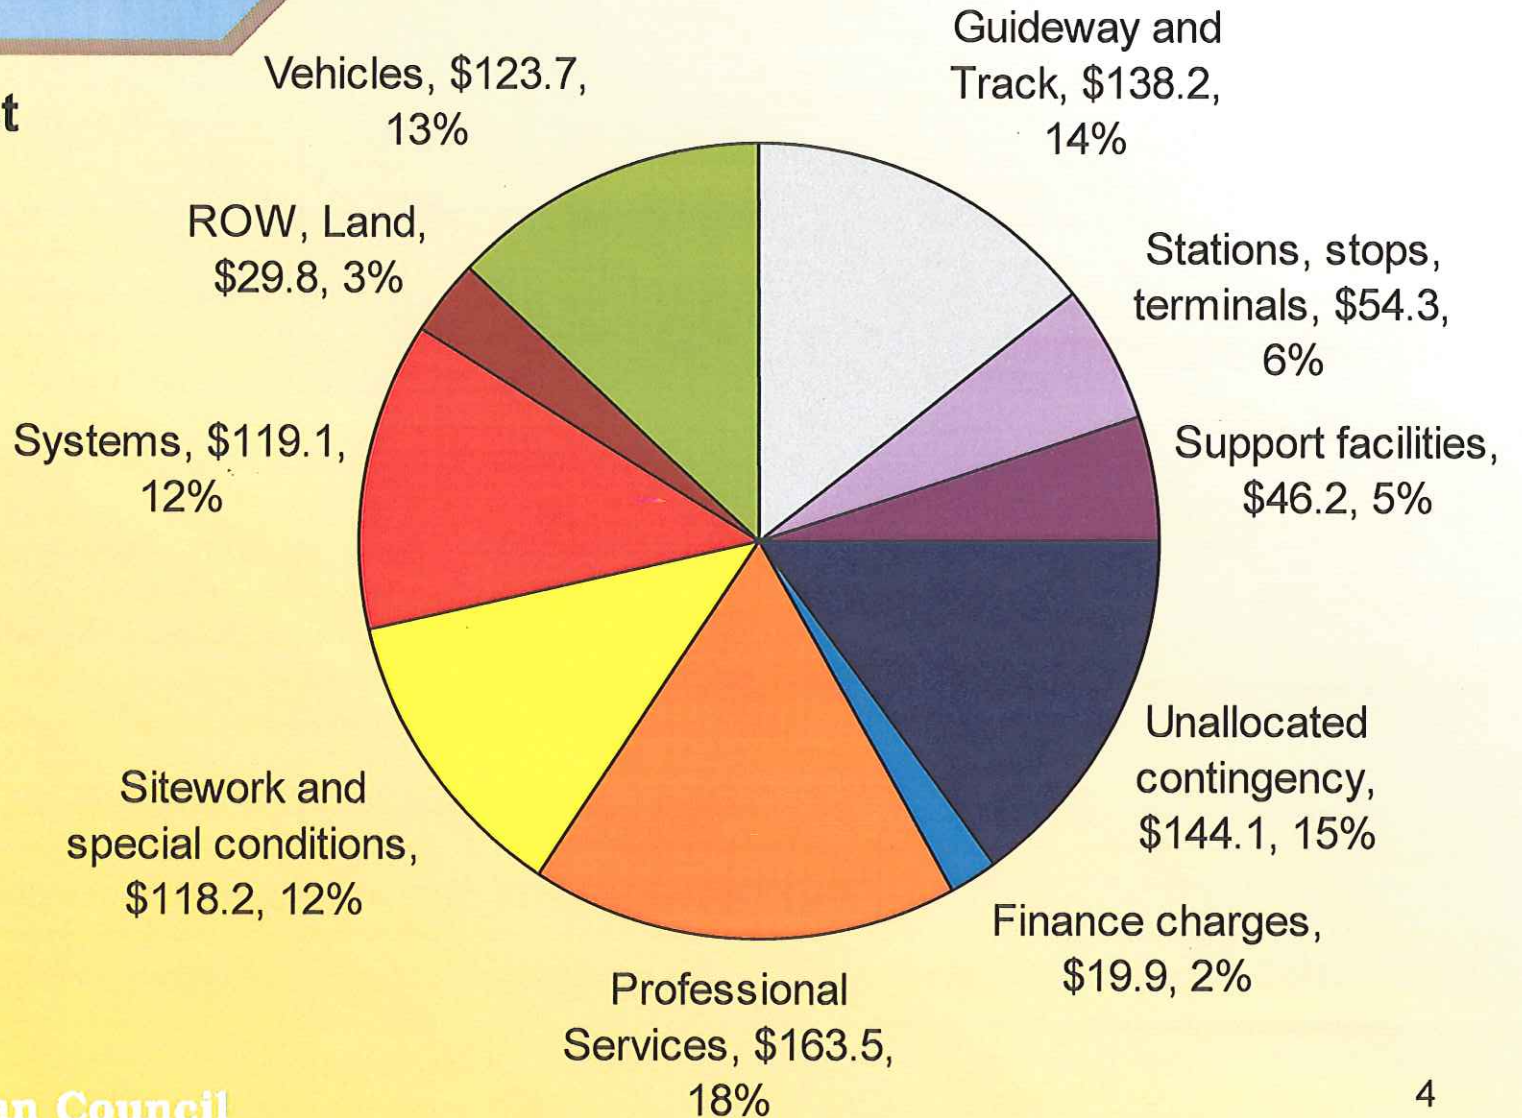

Project Schedule

FTA Grants Entrance into Prelim Engineering (complete)	14-Dec-06
FTA Issues Record of Decision (ROD) (complete)	18-Aug-09
FTA Approves LONP for Adv Utility Relocation (complete)	26-Aug-09
CCPO Advertises Advanced Traffic Improvements (complete)	17-Dec-09
Infill Stations EA Publication (complete)	11-Jan-10
Infill Stations EA Closing Date (complete)	10-Feb-10
FTA Issues NEPA Finding for Infill Stations	26-Feb-10
FTA Approval to Enter Final Design	Late Mar-10
CCPO Submits FFGA Application	Late Mar-10
FTA Execution of FFGA	01-Sept-10
Begin Revenue Service	2014

Major Procurement




- **Light Rail Vehicles**
- **Civil East**
- **Civil West**
- **Systems**
- **Operation and Maintenance Facility**

BOLD= >\$125 million contract estimate

Construction Contract Packages


Central Corridor Light Rail Transit

- Advanced Traffic Improvements
- **Civil East Construction**
- **Civil West Construction, including Washington Avenue Bridge (WAB)**
- Operations and Maintenance Facility (OMF)
- Systems
- Fare Collection System

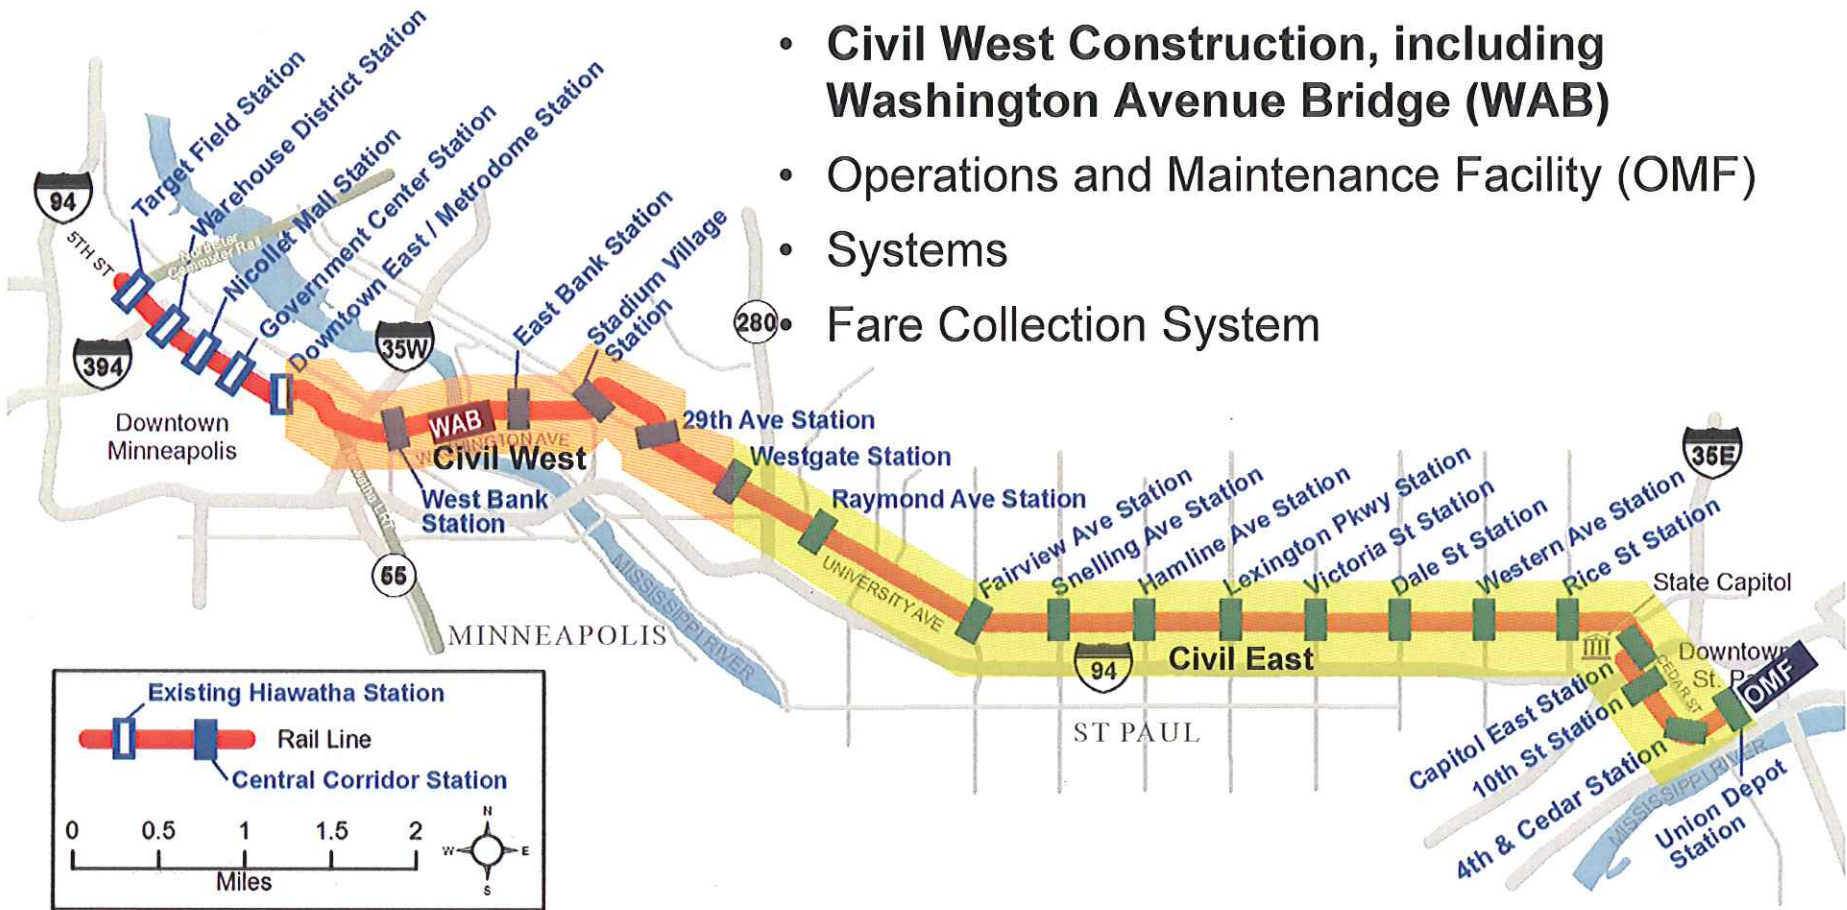

Split Side Platform Station

Signalized Pedestrian Crossing

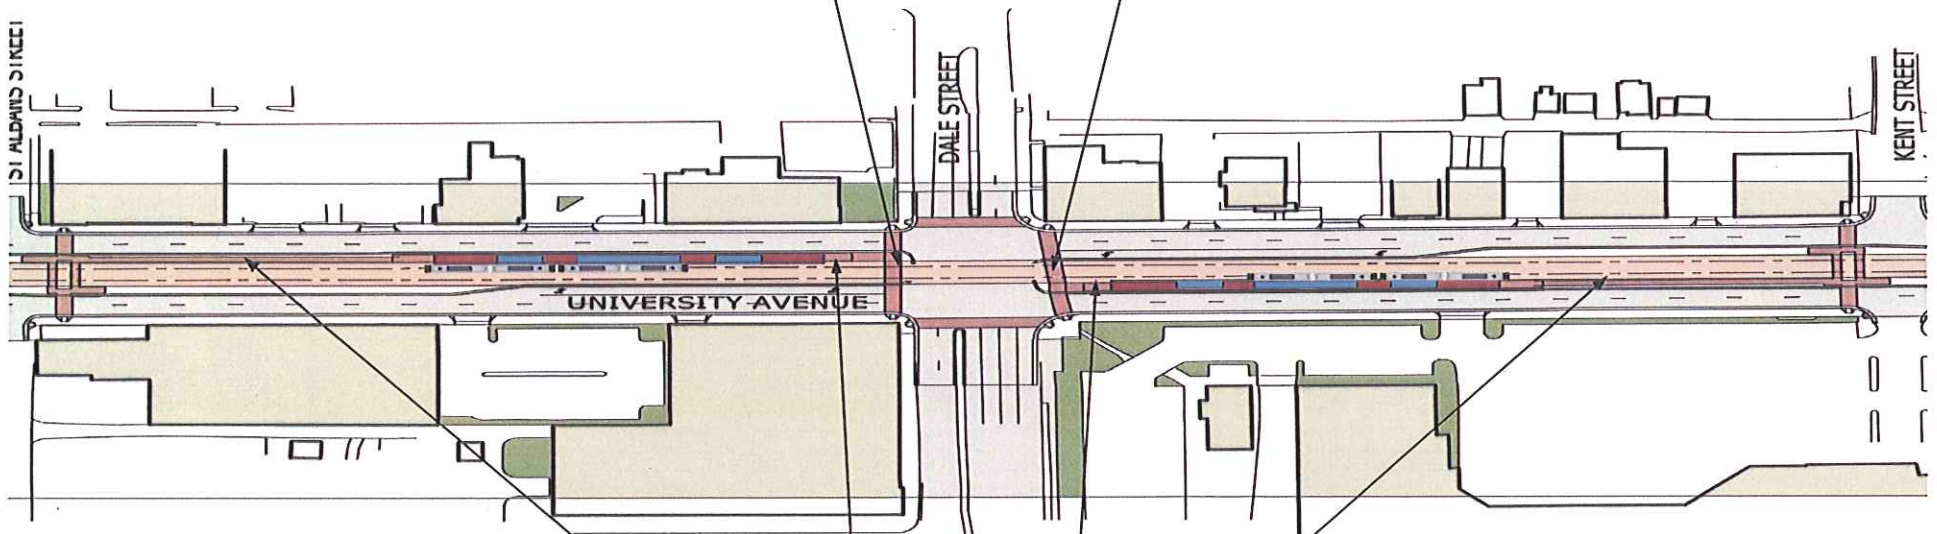

Platform Access

Central Corridor
Light Rail Transit

Parallel Side Platform Station




**Central Corridor
Light Rail Transit**

Rice Street Station



**Central Corridor
Light Rail Transit**

North Capitol Steps Area

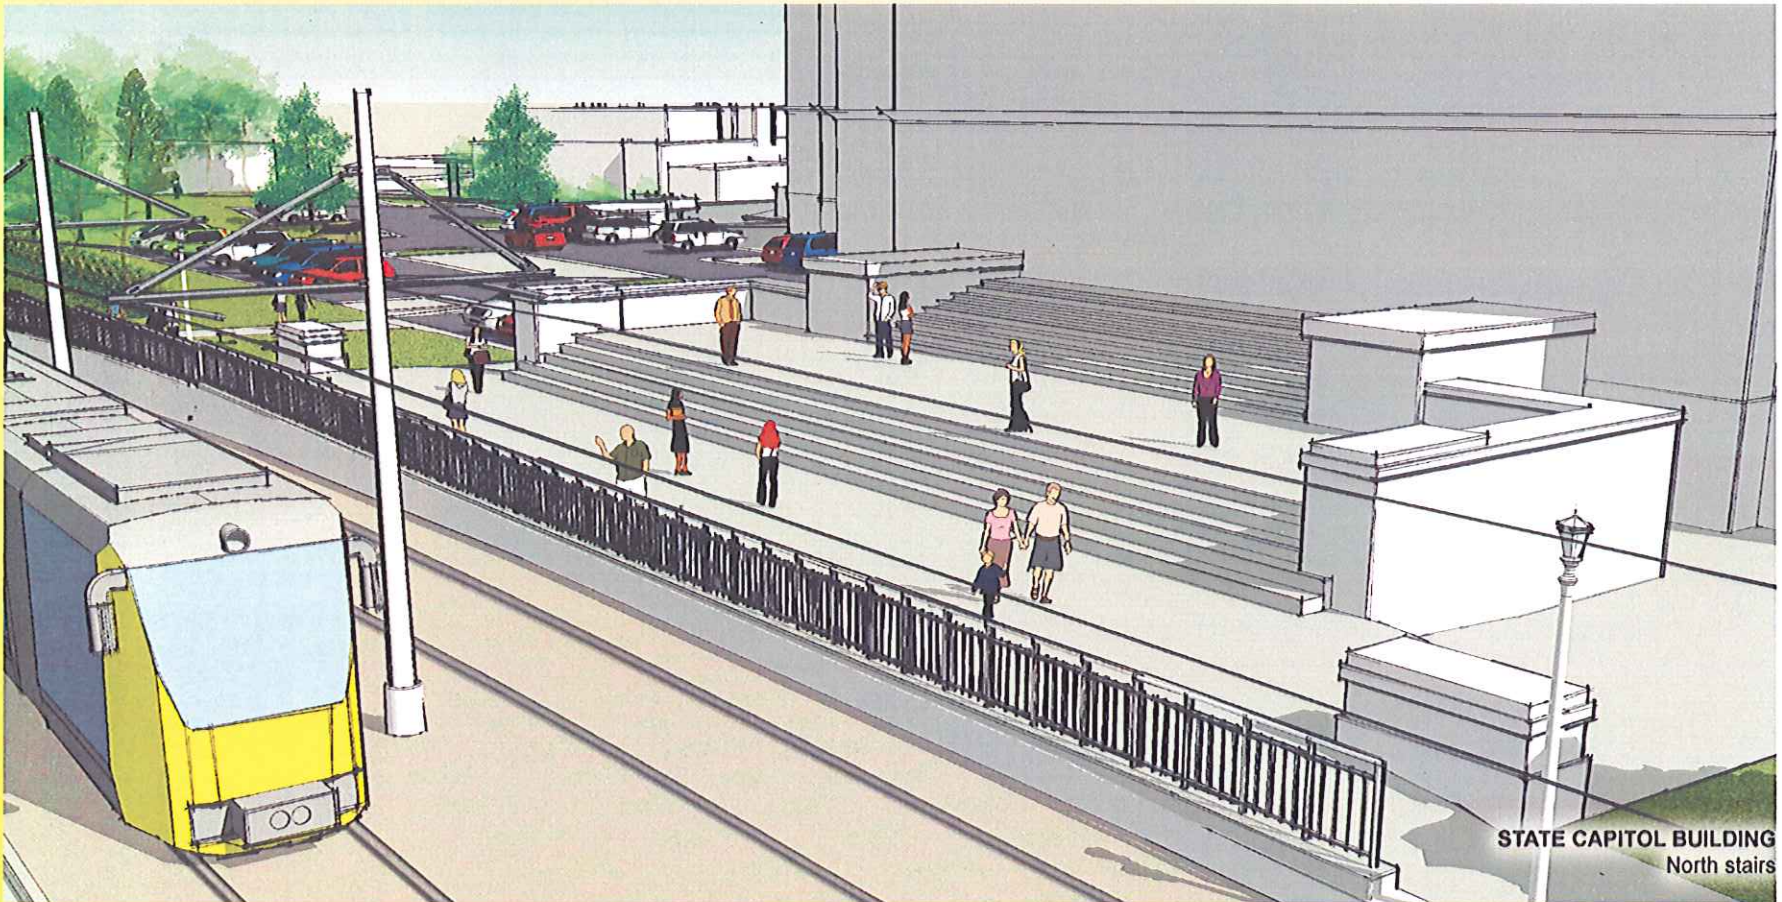

STATE CAPITOL BUILDING
North stairs

**Central Corridor
Light Rail Transit**

Capitol East Station



CAPITOL EAST STATION
Robert Street looking south

**Central Corridor
Light Rail Transit**

Next Steps Civil East Procurement

March 5

- Release bid documents

April 30

- Open bids


June 23

- Award bid

July

- Start construction

Civil East 2010 Work Utility Relocation

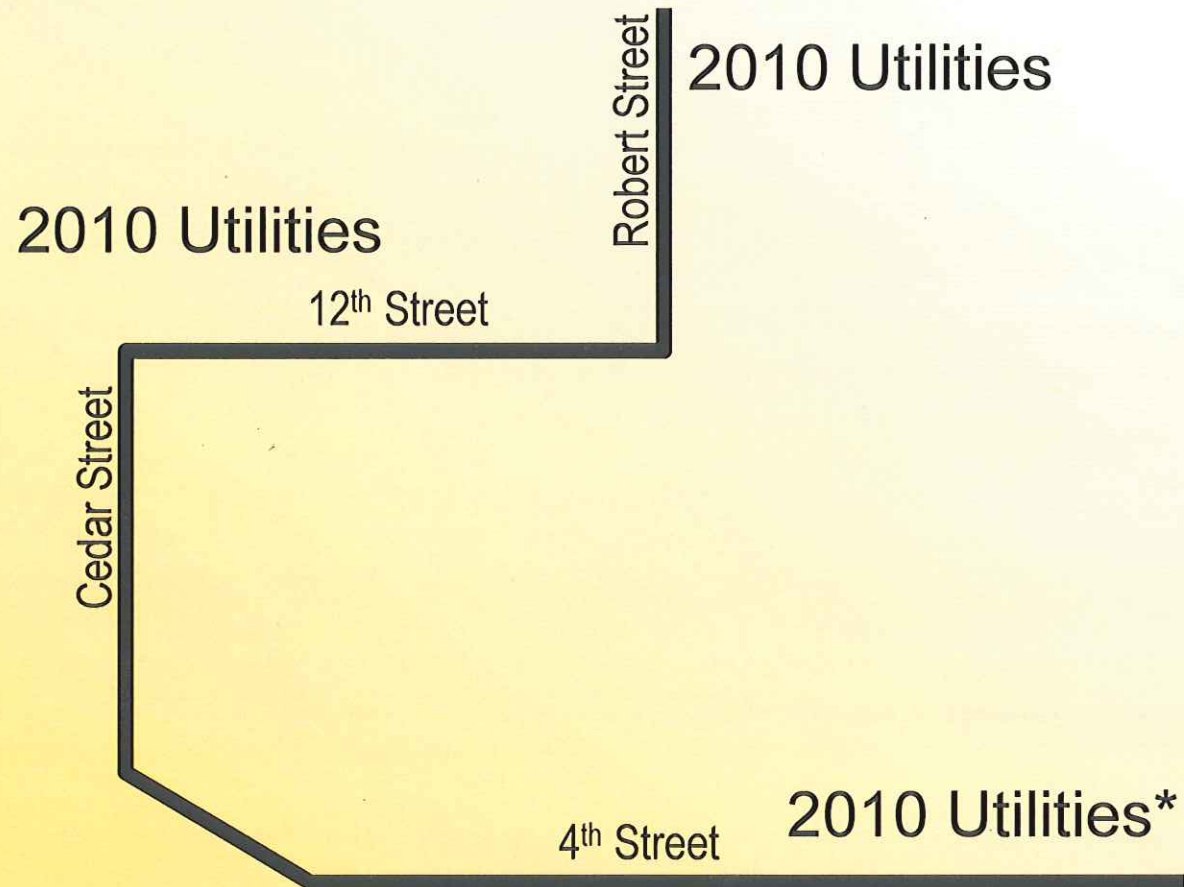

* Complete utility relocation started in 2009 under Advanced Utility Relocation contract

Central Corridor Light Rail Transit

Summary 2010 Milestones

March

- FTA approves entry to Final Design

Spring

- CCPO advertises construction packages

Summer

- Met Council awards construction packages

Fall

- FTA awards Full Funding Grant Agreement

Central Corridor Light Rail Transit

More Information

Check out our website:

- www.centralcorridor.org



Contact Central Corridor Project Office:

- 540 Fairview Avenue North
St. Paul, MN 55104
- Comment Line: 651-602-1645
- Email: centralcorridor@metc.state.mn.us
